

In Depth: The Kickoff Meeting

The build process is four stages and you'll walk through them one by one.

Starting with design, you can describe this as when we *finalise the customer experience of the agent*. Our designers will consume the FAQ information provided and make the agent come to life.

We'll run through the flows, kickoff telephony integration and the client will get to choose their voice.

This is also the final opportunity to make any changes to what you want to build before we hand over to engineering.

Build Process

Build Process

We follow a tried and tested, four stage process that results in a highly successful voice assistant extremely quickly.

Design

Build

Test

Go Live

Build Process

Design

Build Process

Design

Build

Test

Go Live

PolyAI Deliverables

1. Provide technical resource to work with you and your vendors on integrations
2. Agree and finalise the scope
3. Dialogue designer builds the call flows, writes the content and if applicable, trains the voice actor

Client Deliverables

1. Structured FAQ data
2. Complete API documentation and testing environments
3. Complete SIP workbook
4. Provide contacts for requested personnel including a project manager and introductions to key vendors, including a telephony vendor
5. Select a voice
6. Confirm and lock down the virtual agent scope — this may be the last chance to add features until after go live

In Depth: The Kickoff Meeting



We often describe the ‘build’ stage as a quieter stage where the PolyAI team are ‘heads down’.

We’ll still want the client to support on weekly meetings and to motivate their telephony supplier.


It’s good to explain how we’ll still fill this period by introducing the client to:

- how to interpret dashboards
- how to talk about our agents with contact centre staff
- talk about design methodology
- introduce them to self serve tools
- introduce the BAU support process.

 All of these are coming in new decks in collaboration with CS soon, but even though we don’t yet have content, you should cover off these topics in this period.

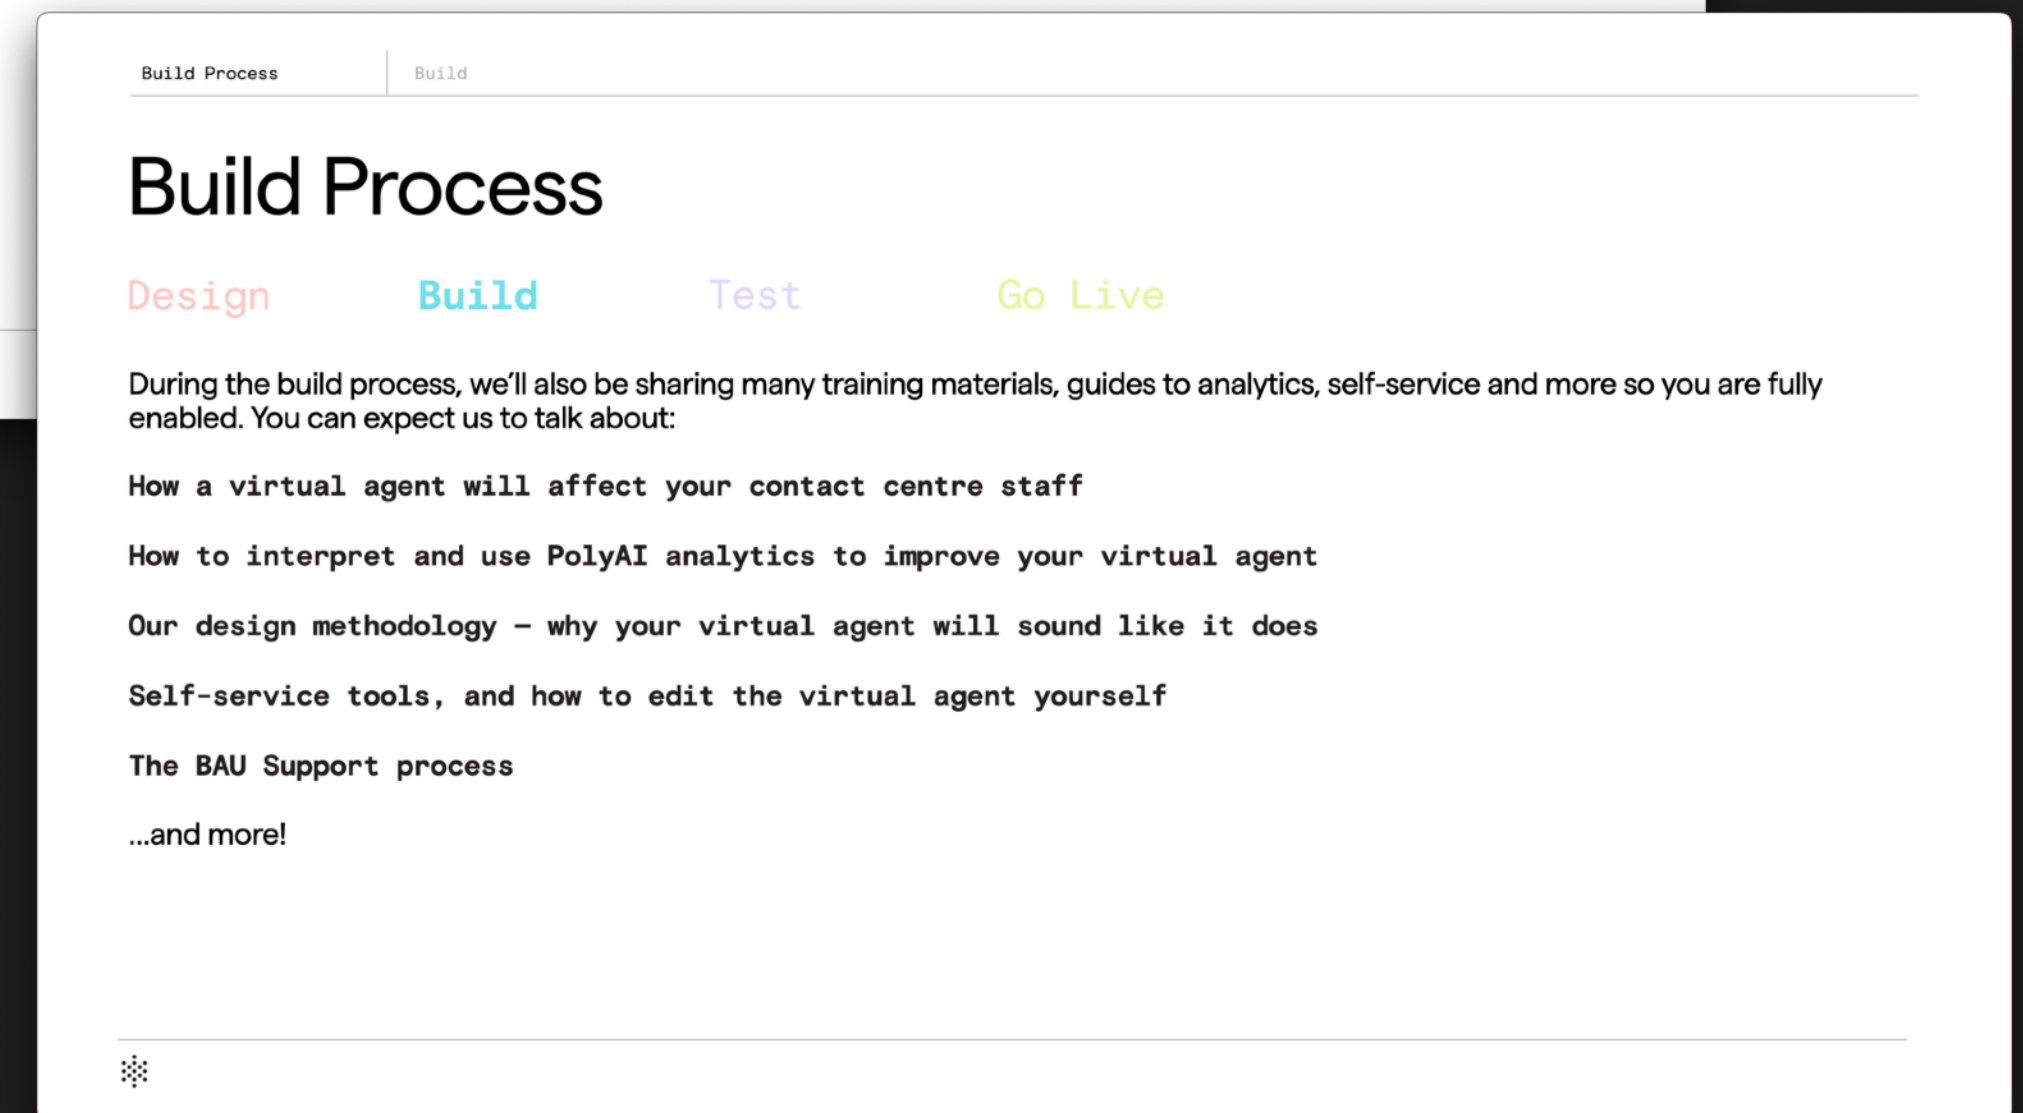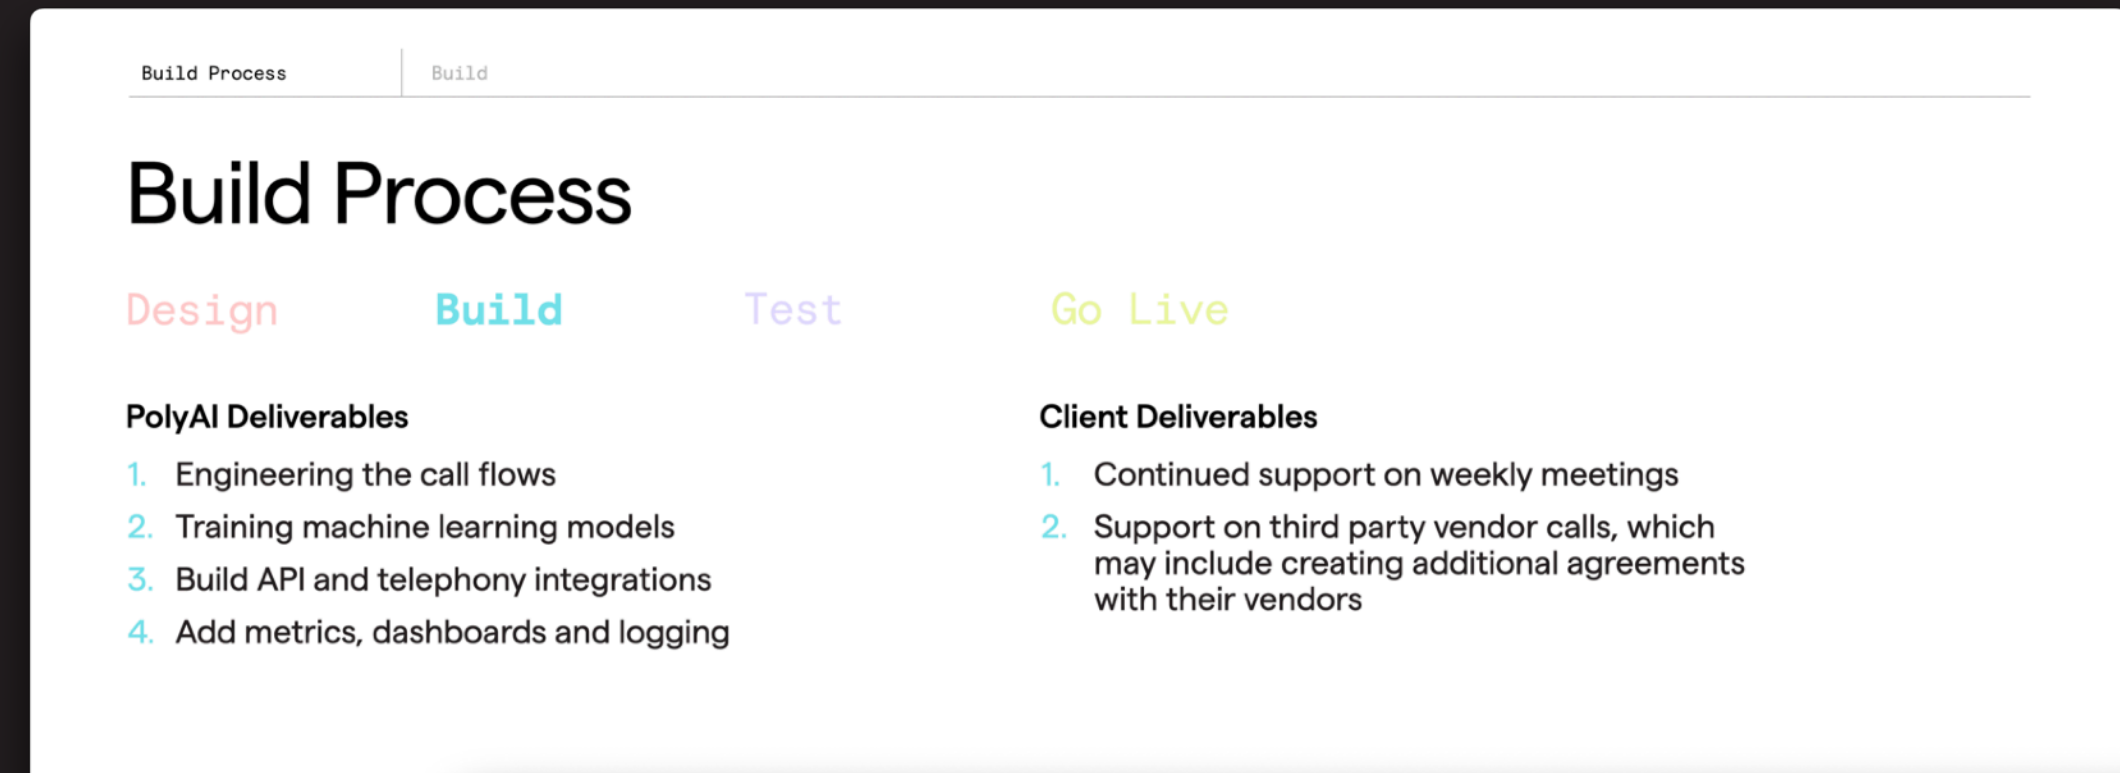

In Depth: The Kickoff Meeting

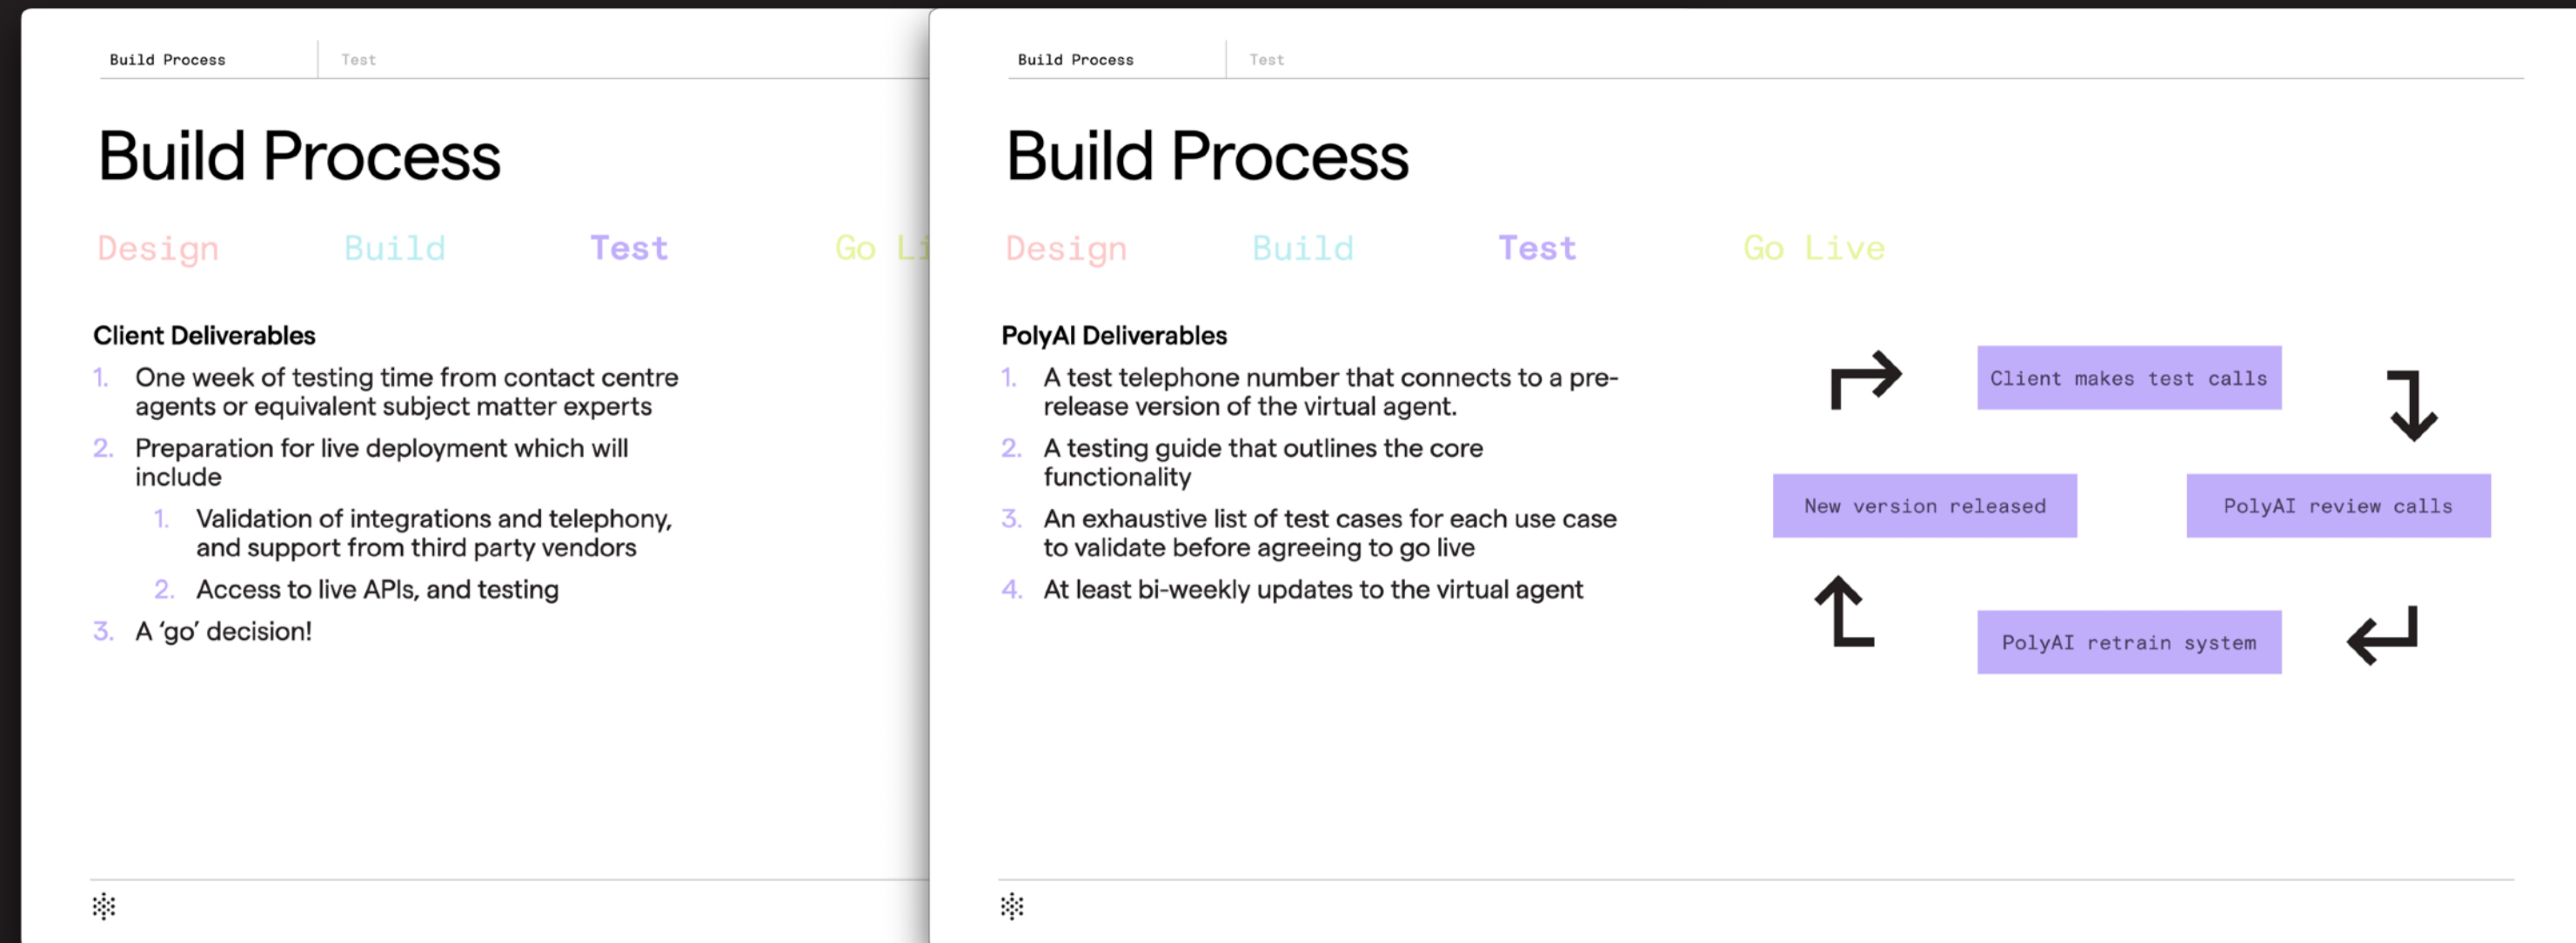

We like to describe UAT as *where the fun starts*. This is what most of our clients enjoy, getting to experience the PolyAI virtual agents for the first time. For this section of the deck, read through the deliverables and explain we'll be making updates *nearly daily* and will be really high touch.

You can describe how we'll provide *a comprehensive test plan to ensure the agent launches well*, as well as a *guide for contact centre staff*, which is the UAT kickoff guide described later.

In Depth: The Kickoff Meeting

It's good to give a brief overview of what to expect on go live day.

This slide includes four examples of how we might roll out. Ultimately, we want more calls as quickly as possible, so build confidence with the client so that they agree ideally to numbers 1 or 2 on this list.

Familiarise yourself with projects that launched in these ways.

Build Process

Go Live

Build Process

DesignBuildTestGo Live

Staggered Rollout

The system can rollout with a percentage of incoming calls. Different clients launch in different ways, for example:

1. **100% on Day One** - some of our customers see the benefit of learning from a high volume of calls
2. **Test on Day One, Launch on Day Two** - for those with new integrations or telephony integrations, it might be safer to start with a small volume on day one, before moving to 100% on day two.
3. **Slow ramp up** - Other customers increase the % every day. We usually aim to be at 100% at the end of week one
4. **Launch per business line** - Finally, it may be possible to launch with a subset of customers by enabling only a single inbound phone number or subset of customers, like existing customers but not new ones.

