
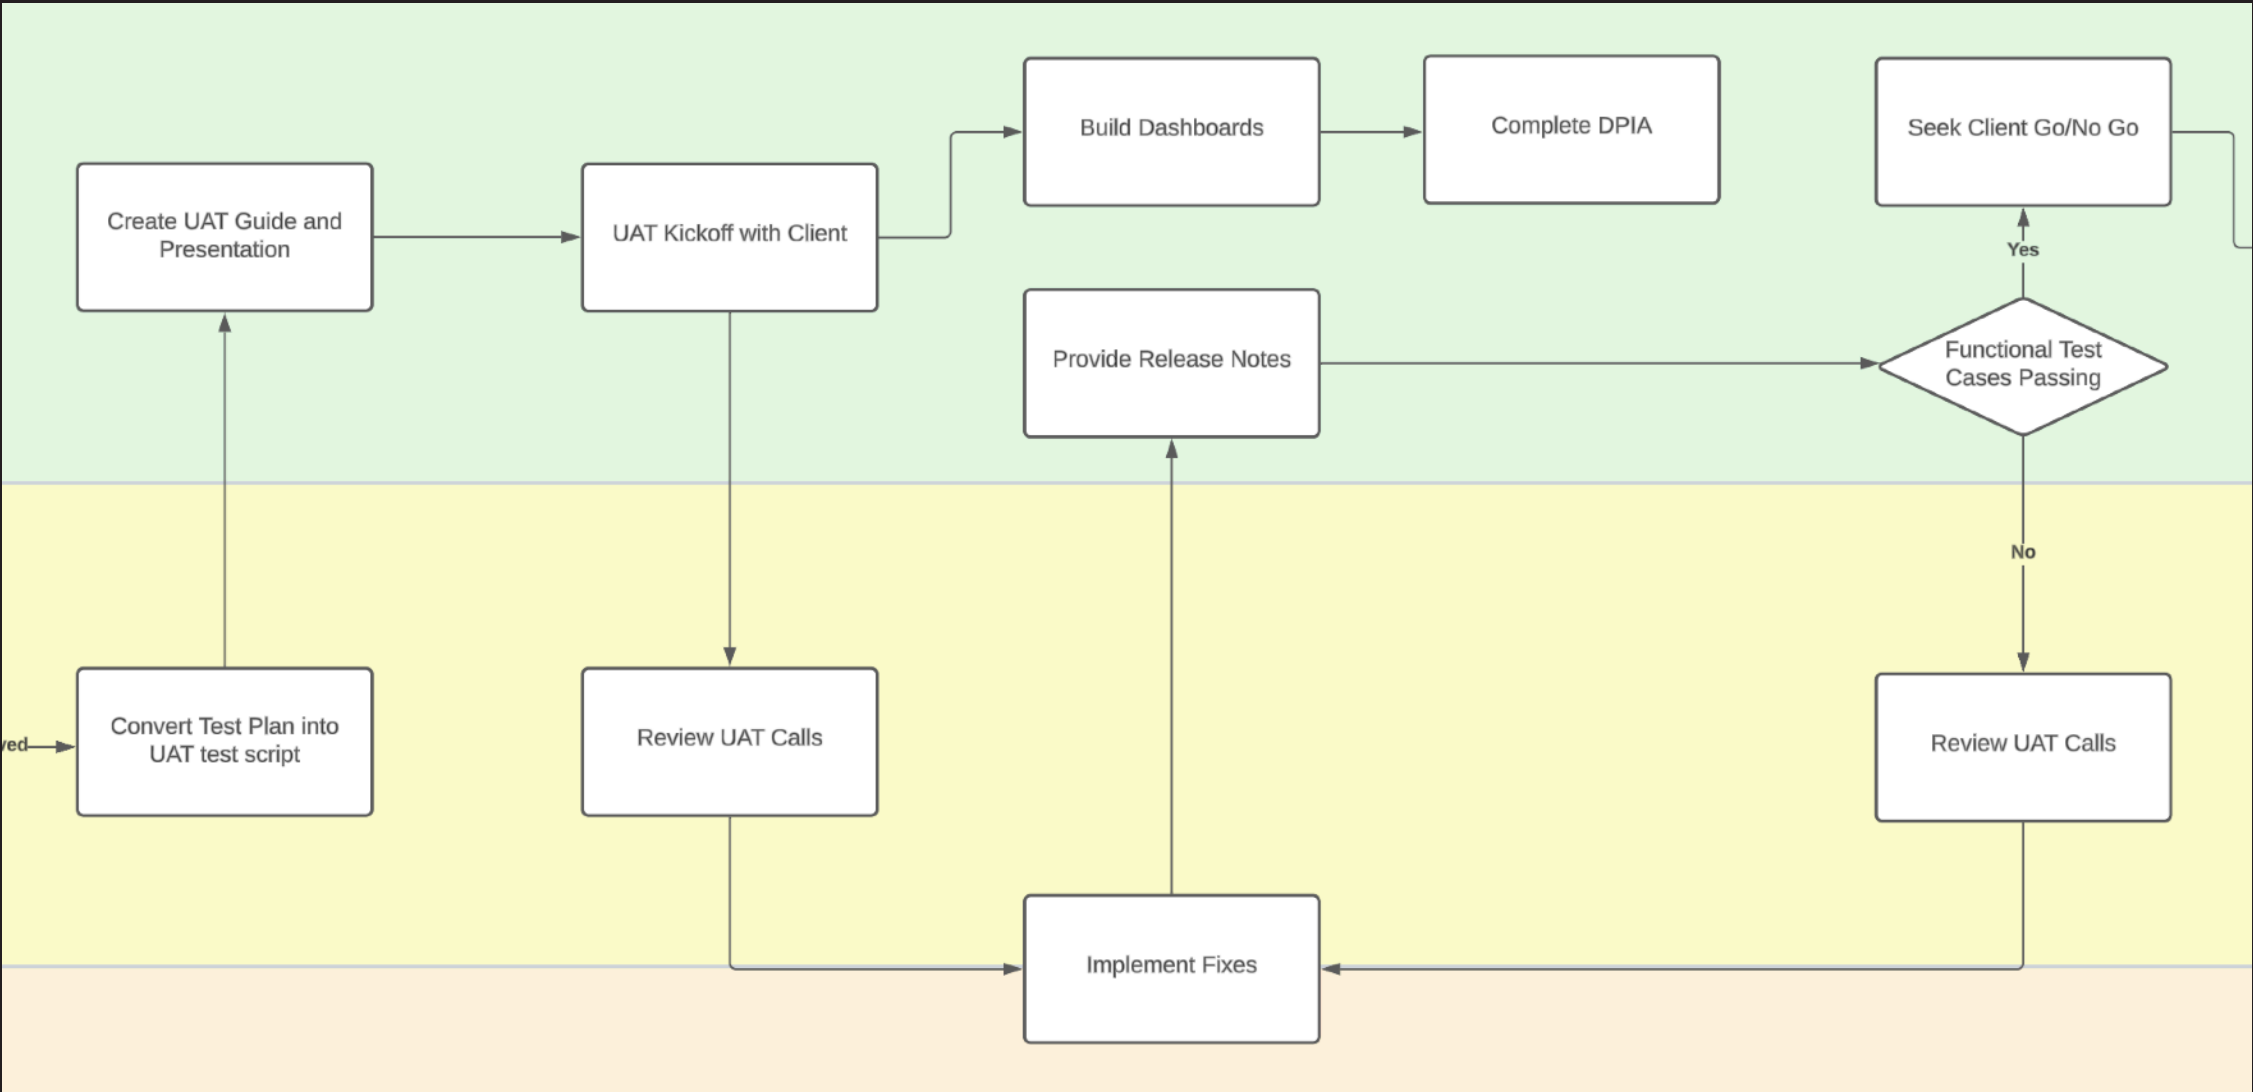


# Deployment Process: UAT ①



## Before UAT

Remember, the client is not here to do QA. Be ready, expect 100% pass rate from the team and expect no less. Prepare the QA sheet for client facing, with scoring using the below criteria. It is your responsibility to make the internal QA sheet client-friendly for UAT. See an example here. [🔗](#)

## UAT Kickoff

Use the UAT slide template to explain the difference between functional and behavioural testing and plan testing. Reassure the client some things won't work but that's normal. You'll be making many changes over the period to improve the system. We'll listen to every call but priorities the bad CX fails.

## Scoring Functional Testing

This is how to score a functional test you complete.

### As Designed - Perfect

The outcome of the call was as designed. For example, a visitor who should be granted access was granted access. The user was understood first time, and the CX was good.

### As Designed - Imperfect


The outcome of the call was as designed. For example, a visitor who should be granted access was granted access. However, the experience was not perfect. The outcome was correct, but the user may have had to repeat themselves.

### Fail - Good UX

The outcome of the call was not as intended. For example, the agent transferred a user to a human operator despite the fact the visitor was authorized to enter and the API provided correct information. However, the user experienced a seamless experience, such as a fast transfer to a human.

### Fail - Bad UX or Incorrect Admission

The bot did not behave as intended, and the experience was bad, for example, the user was stuck in a loop and then transferred. Or, PolyAI mistakenly admitted a non-authorized visitor.

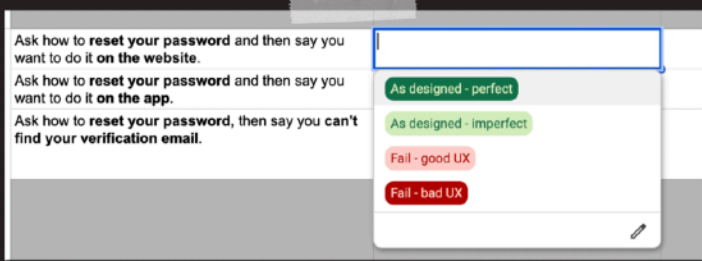

## Testing Tips

There are two types of testing. We strongly recommend keeping these testing types distinct.

### Functional

#### Does the bot behave as expected?

Use the PolyAI UAT sheet to validate all test cases and annotate them using the included scoring scheme on the next slide.

When PolyAI update the agent, we will let you know which cases to re-test.

All cases should be marked as 'As Designed' for Envera to approve go live, unless we mutually agree.



### Edge Case

#### Can I break the bot?

Run some edge case testing, to ensure the agent behaves appropriately.

We don't look for perfect pass rates here, as they should be rare cases, but want to offer Envera comfort in deploying the bot.

# Deployment Process: UAT ②

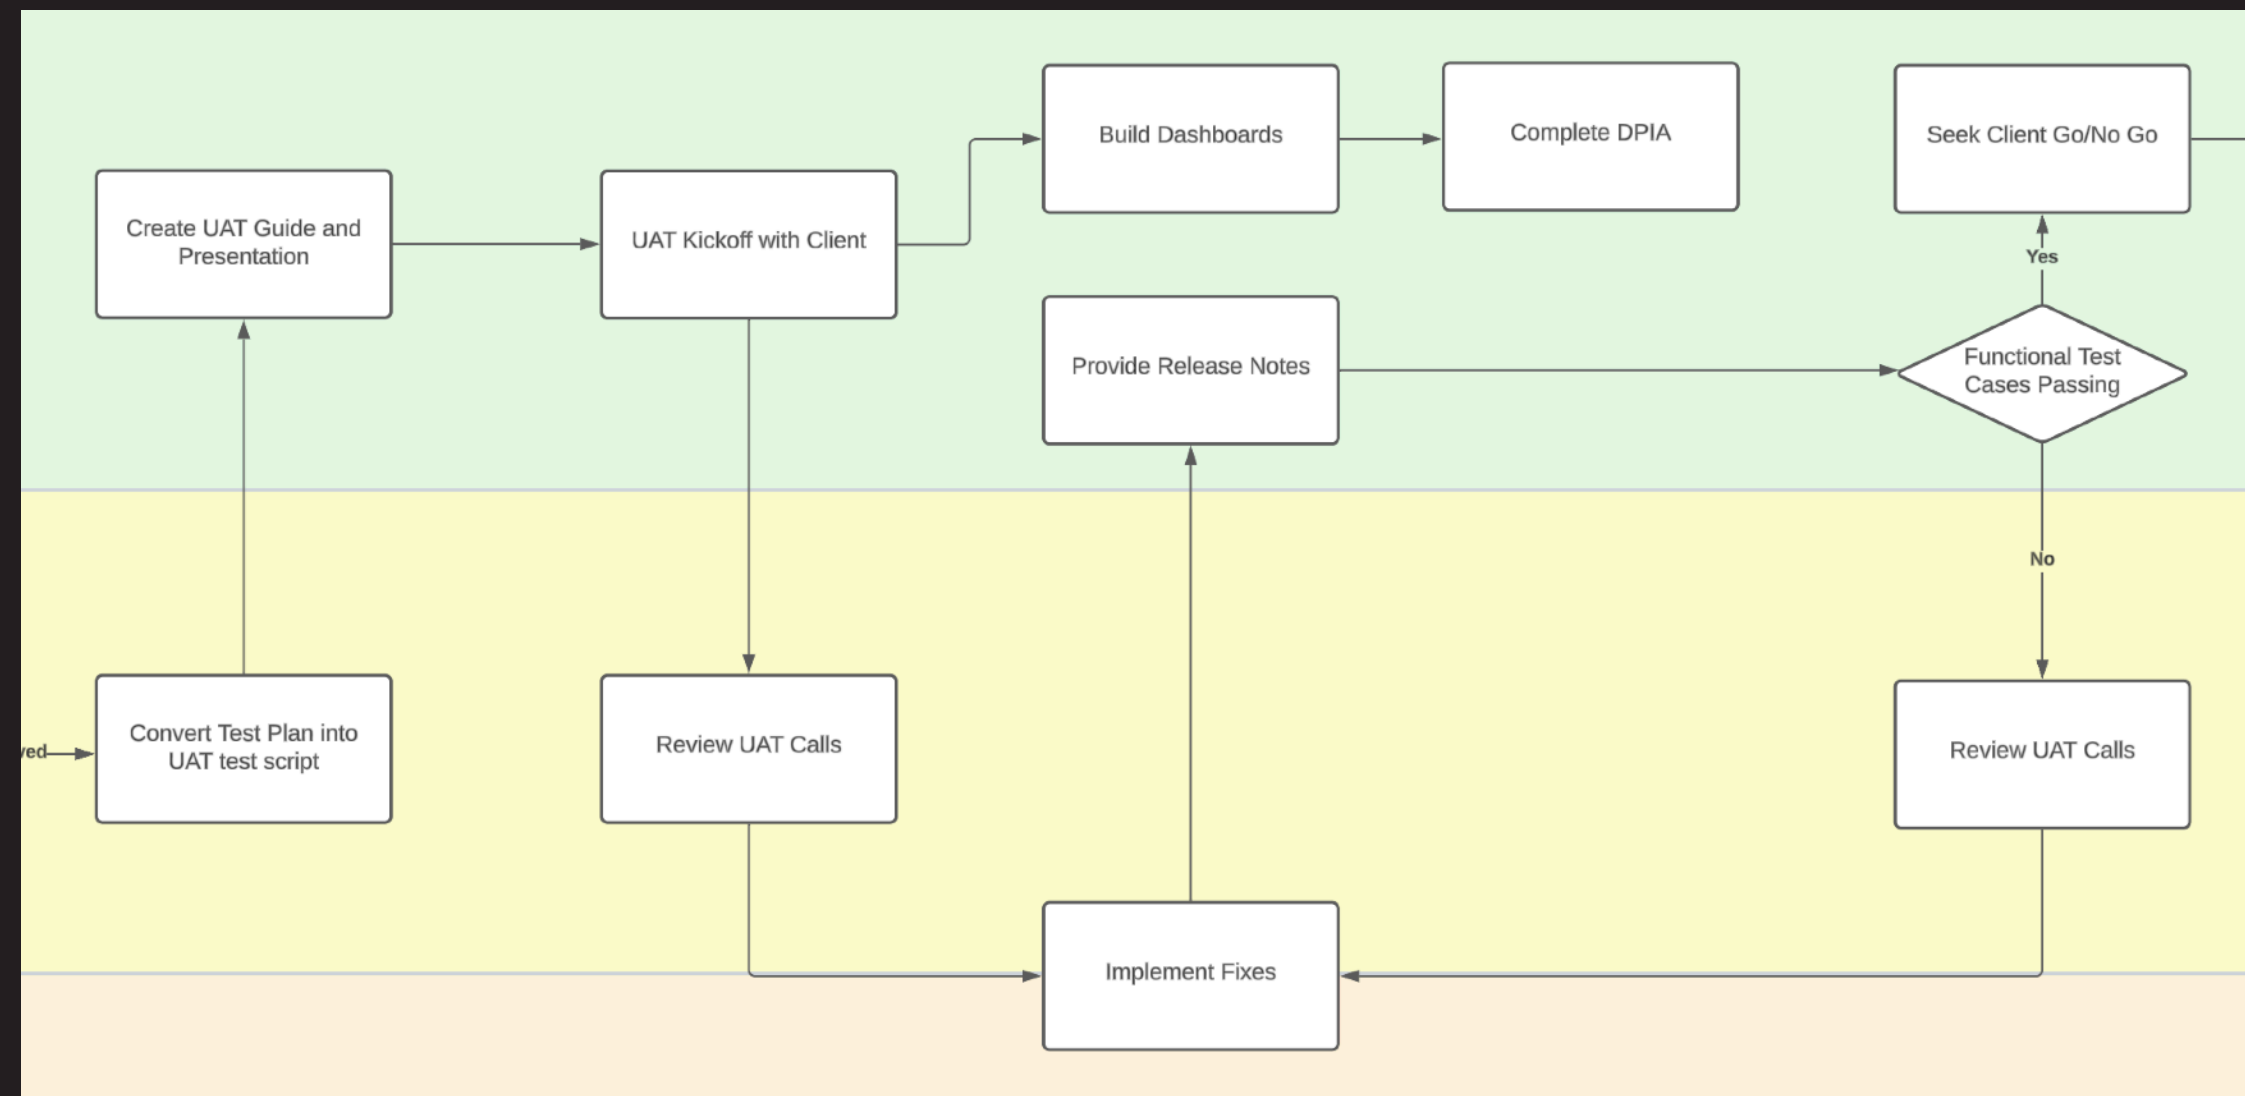

## During UAT

Keep the testing sheet open. Check in frequently and ensure the Agent Designer and engineer are live commenting on test cases and listening to calls. You can use PolyAI ticket numbers to reference issues. You can also prioritise them in real time.



There is more advice on how to run the day to day of UAT on page X.

## The end of UAT

If you have provided good release notes, active check-ins and explained issues, as well as managed a bug tracker, you will likely have an easy time getting a client to agree UAT is passed, or at least that remaining issues are not go live critical. Use the bug tracker format to prioritise, demonstrating progress.

If you are struggling, try and set a go live 1-2 weeks out. Book daily meetings to rally the client into going live, and plant the suggested date as immovable. If you invite third party vendors, and the people you are relying on to go live, it will create pressure on individuals to hit that go live date.

# Deployment Process: UAT ③

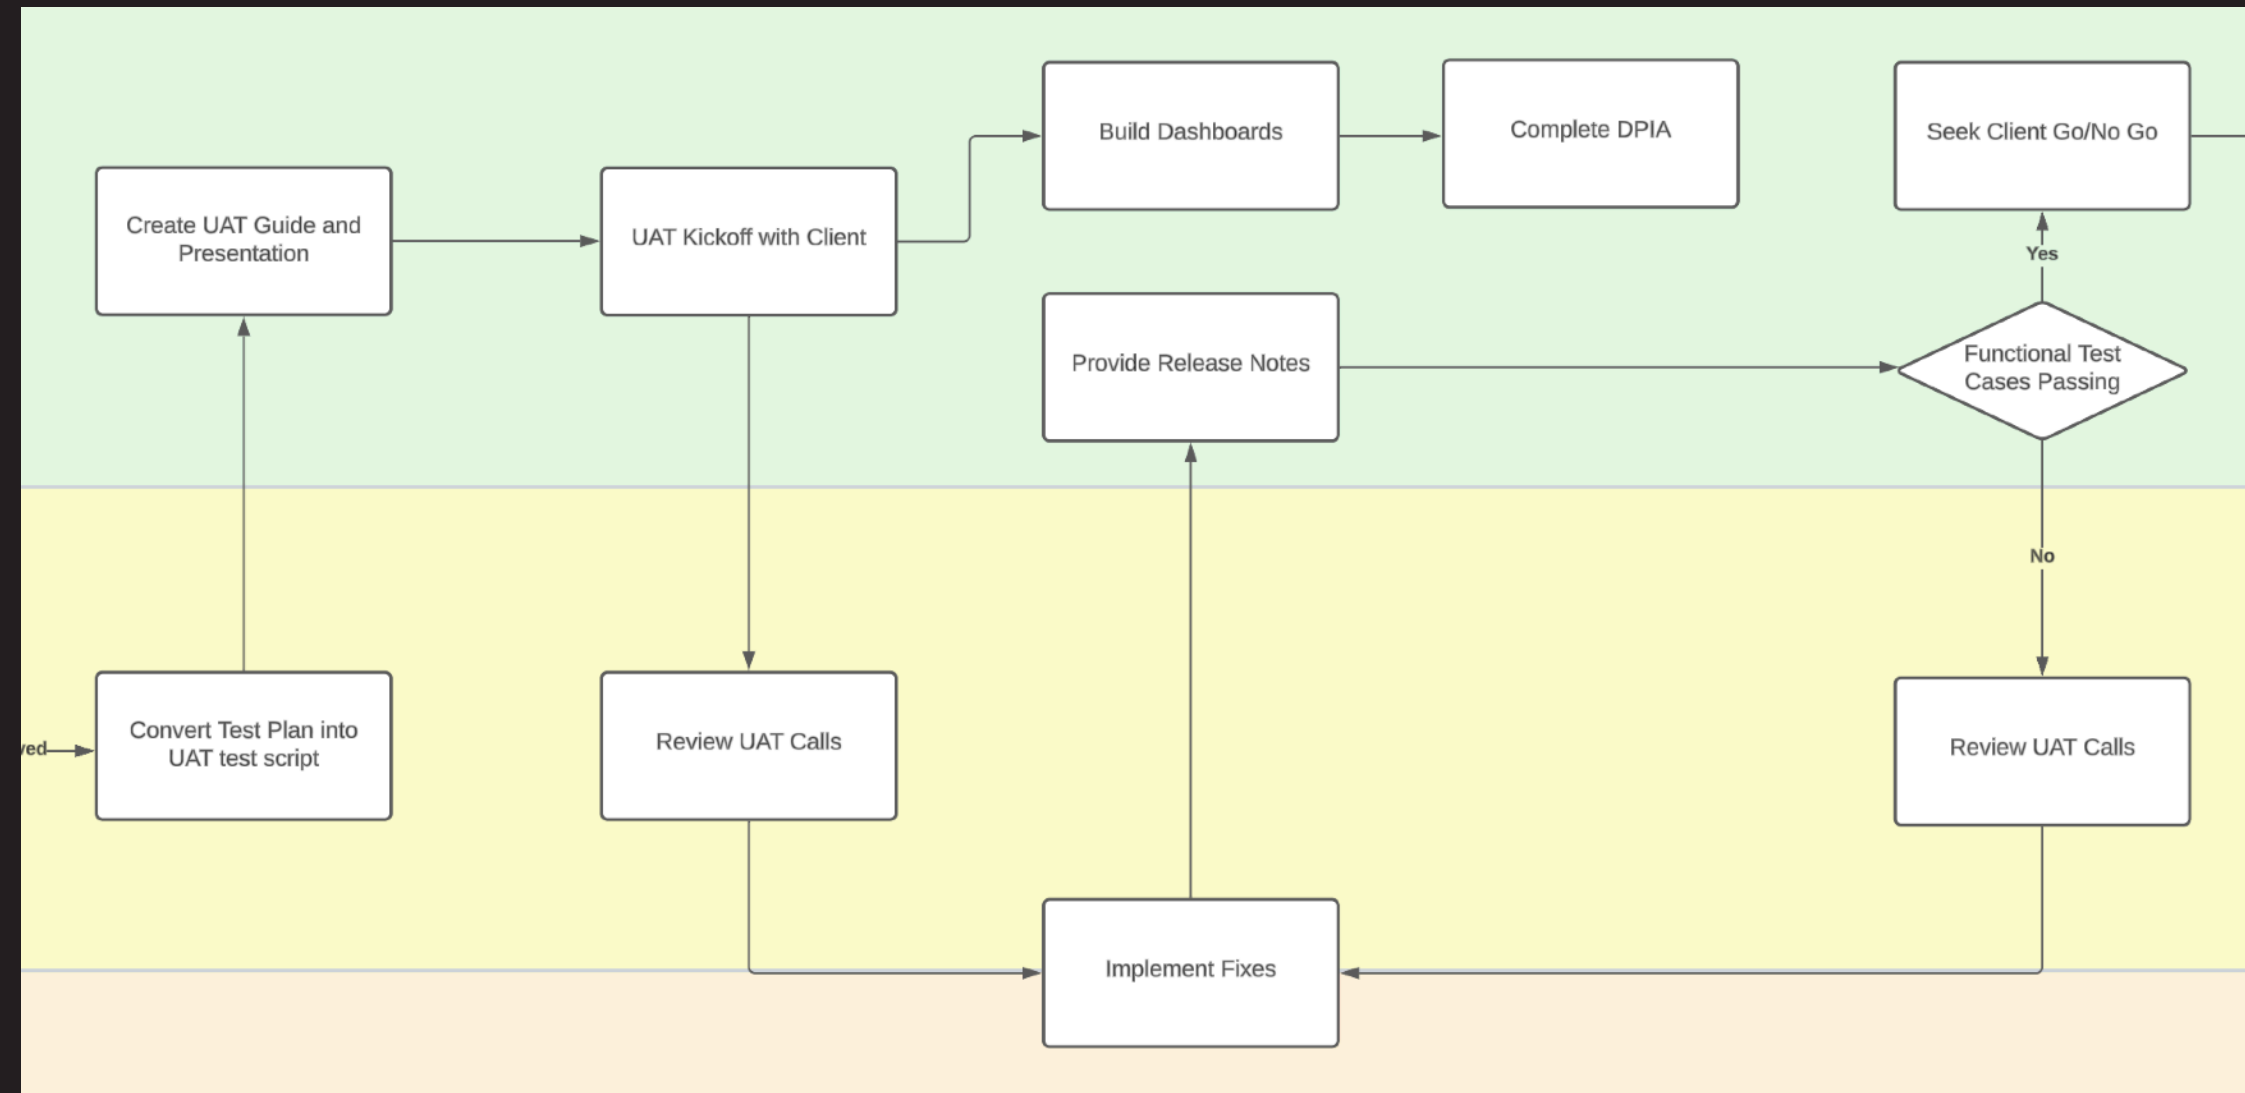



## Dashboards

During UAT, you should monitor that metrics are being written correctly, and added to Luzmo. You might need to ask the engineers to ensure metrics are added to Luzmo.

Advice on building dashboards can be found on page X.



# Deployment Process: Pre-Go Live

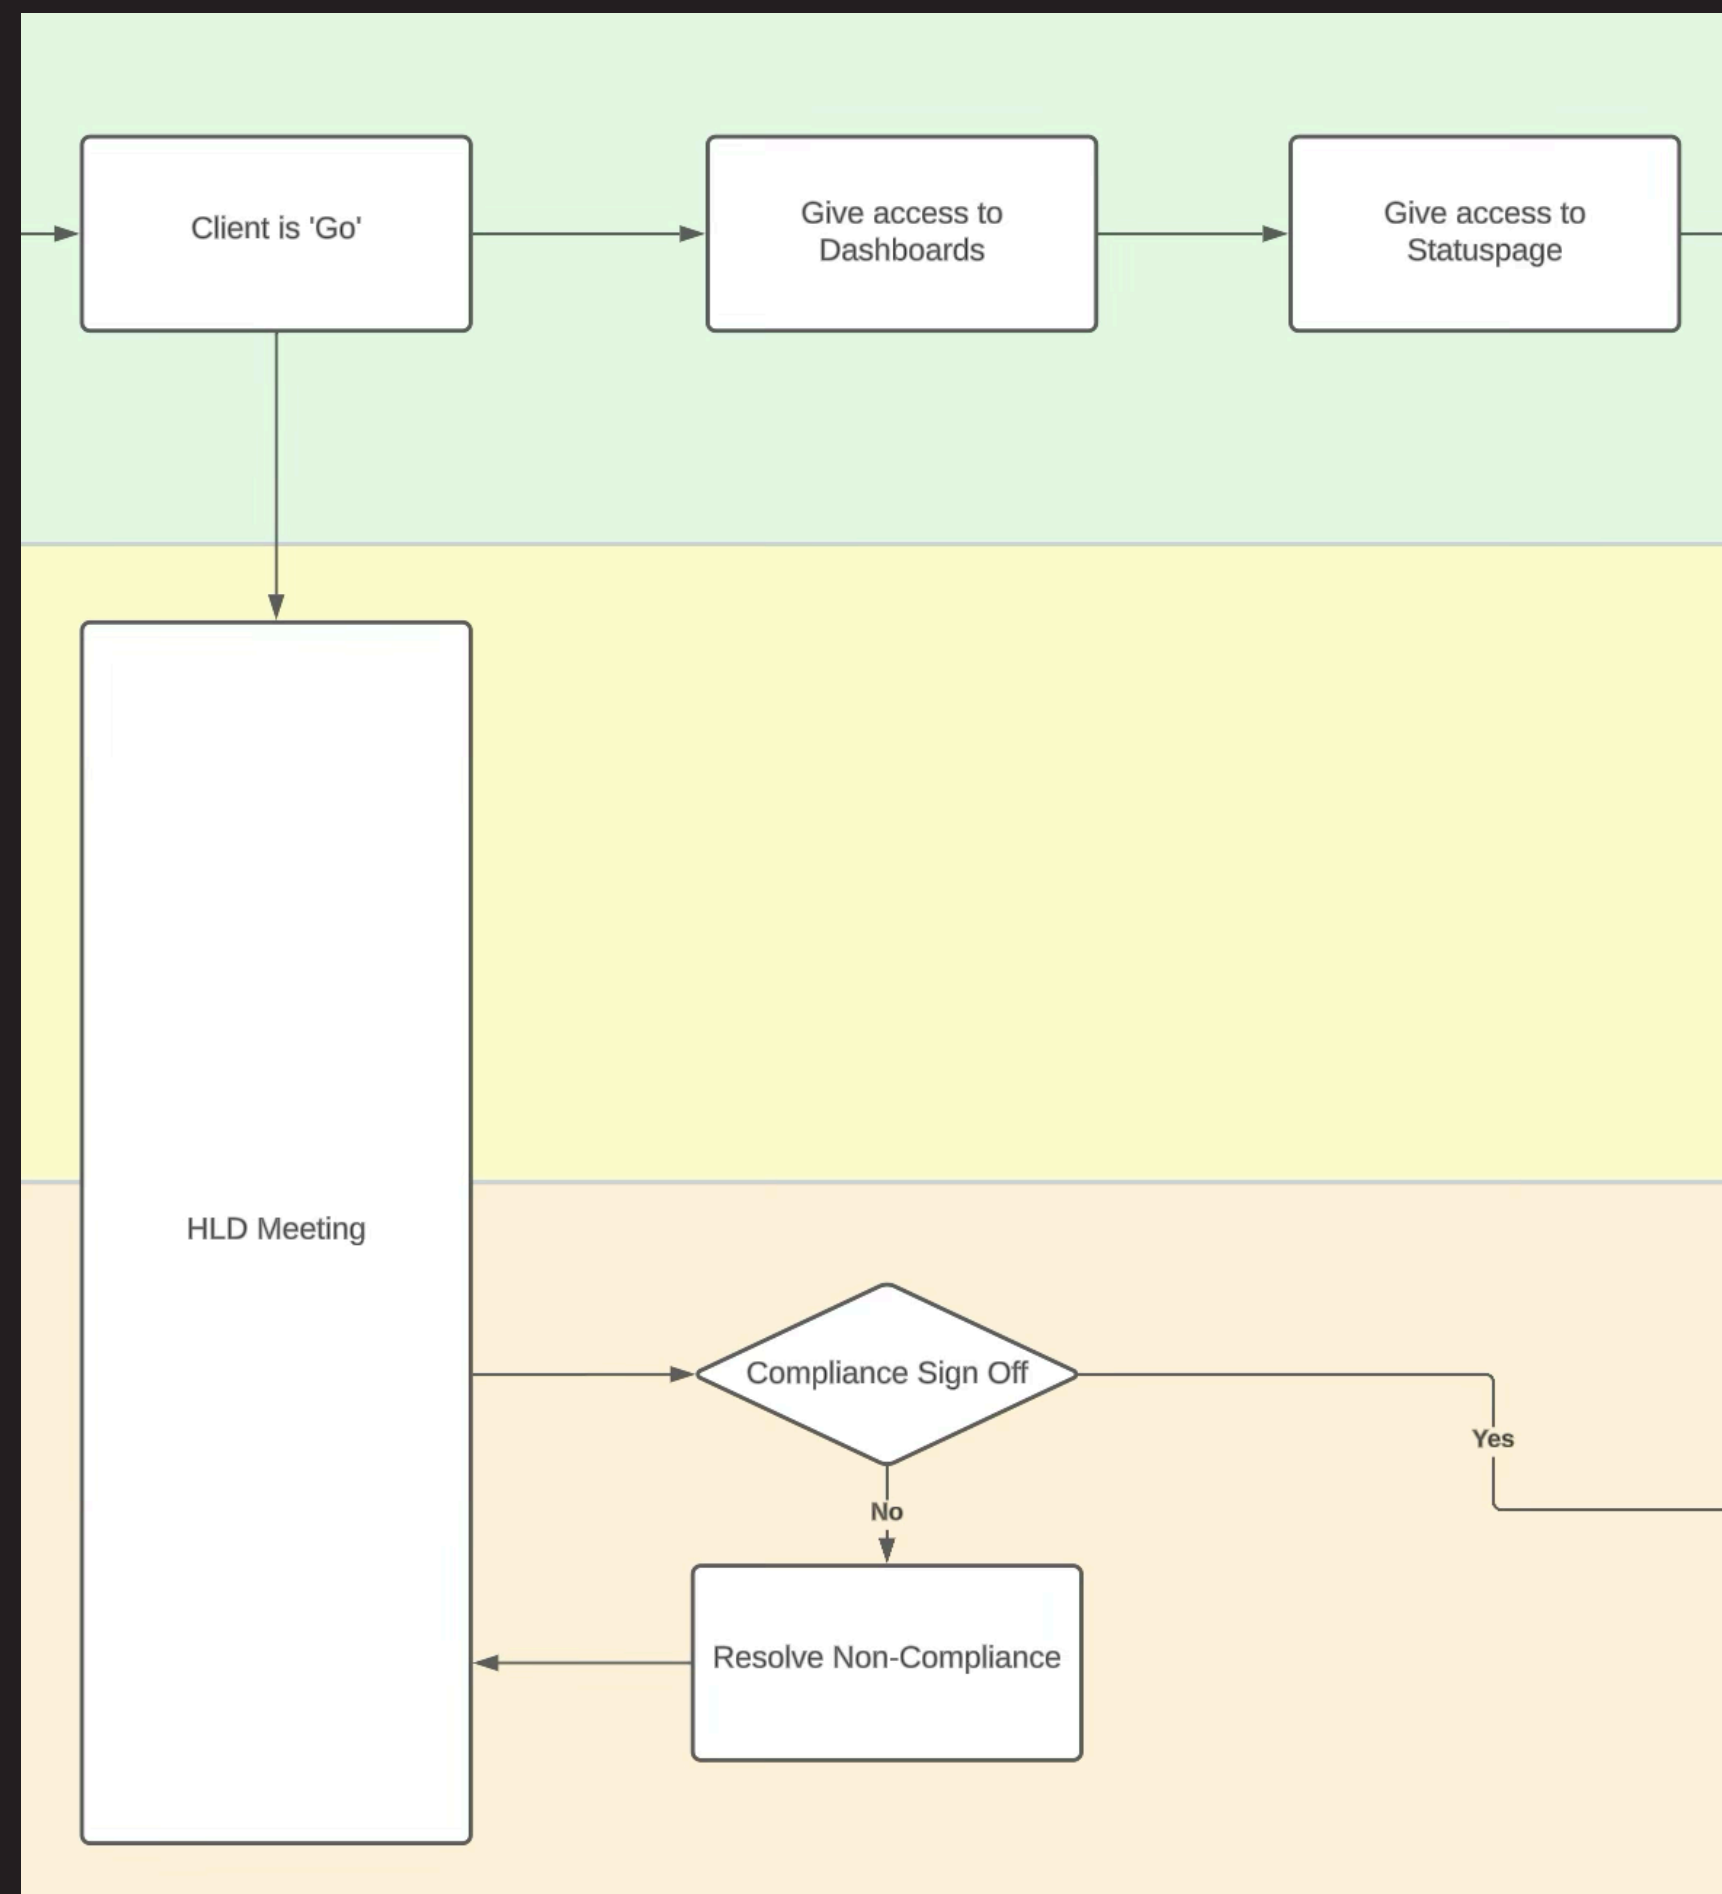

## Once the client says 'Go'

The engineering team will run an HLD meeting. The PSM is optional, but this is a critical internal governance step. Be sure an engineer has written the HLD document in advance of this meeting.

It is important to then **test the live APIs**. This may require setting up a call with the customer to do an end-to-end production test. You should be sure live APIs work before going live.

## Give Access to Dashboards

1. Ask the client for a list of emails who will need access to dashboards
2. Post the list of emails and the region in #studio\_portal\_access\_request channel **and** email the same list to user-access@poly-ai.com. Wait for positive acknowledgement.
3. Add the user to Agent Studio. [🔗](#)



All clients are added to jupiter.polyai.app / jupiter.uk-1.polyai.app, regardless of their project setup. Give them access to custom analytics only on day one. No client should be given access to platform.polyai.app.

## Give Access to Statuspage

Instructions are found here [🔗](#)



# Deployment Process: Go Live

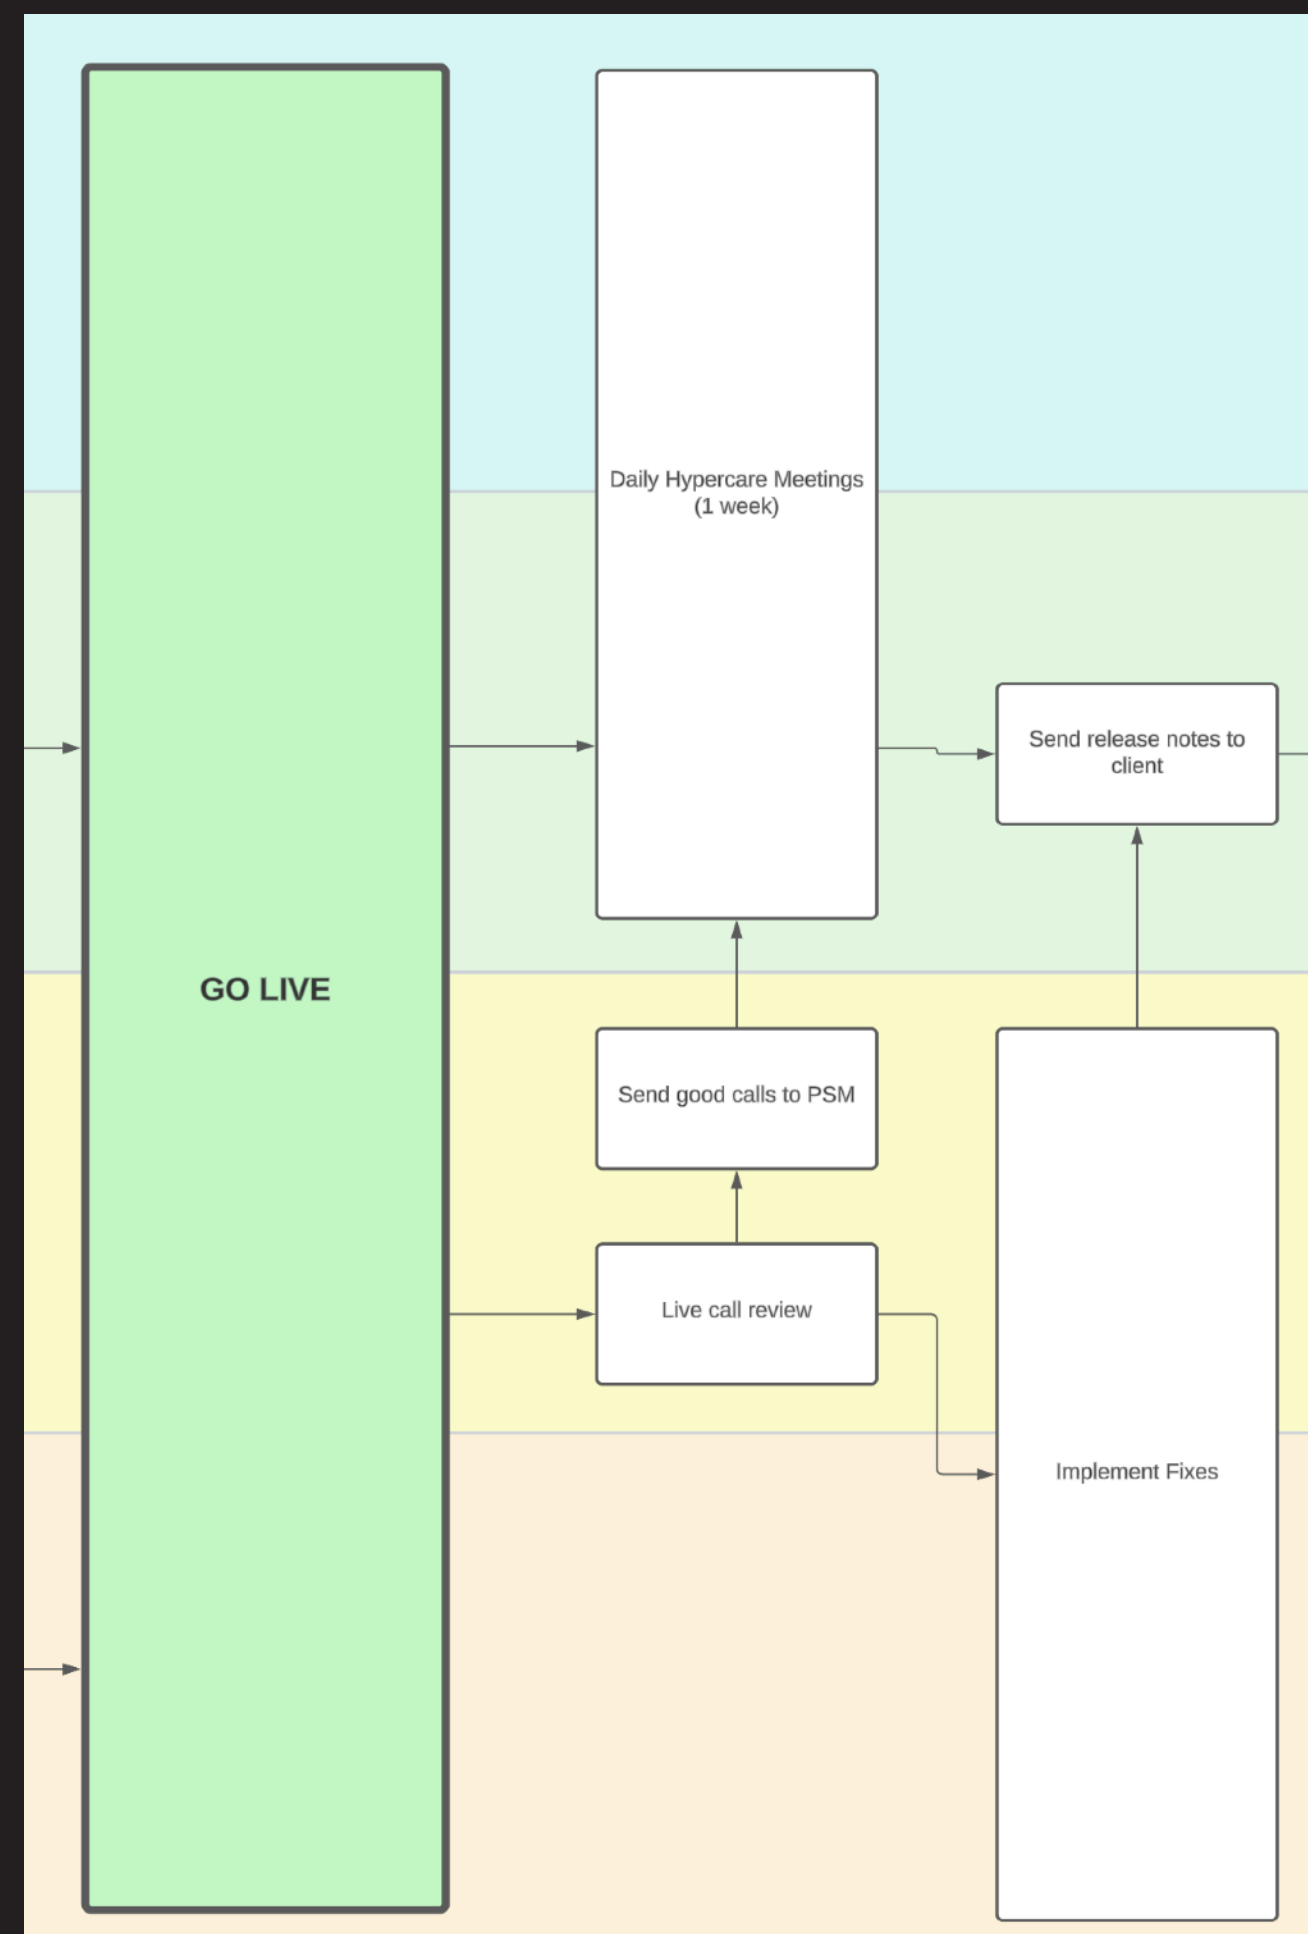

## Go Live Email

You must send an email to the client's main stakeholders, cc Nathan *and* legal, and confirm go live. [🔗](#)

## Post in #general in Slack

Celebrate the team with details of the project, a call recording and more in the #general channel in Slack.

## The Bridge Call



To go live, you should join a longer (2 hour) call with the client to pull the trigger and monitor live calls. This is important as **you want to be the one to play the first good and the first bad call**. If you own and lead this meeting, championing how good the bot is, and mapping improvements onto the bug tracker, you own the narrative. Think of it as an initial hypercare meeting.

## Daily Hypercare meetings

Agree you will run daily meetings for 1 or 2 weeks as soon as possible. The sooner you plant the seed about the duration of this process, the more likely it is to stick. Otherwise, they may extend it forever. In these meetings you should:

- Show and add to a bug tracker
- Send release notes to the clients for every push to live — if you are doing work **show it off**
- Use the dashboard to show KPIs
- Play live calls, including good and bad ones. Pick calls that aren't catastrophic but show out of scope topics or issues you know can be resolved, this helps build trust

# Deployment Process: Shifting to BAU

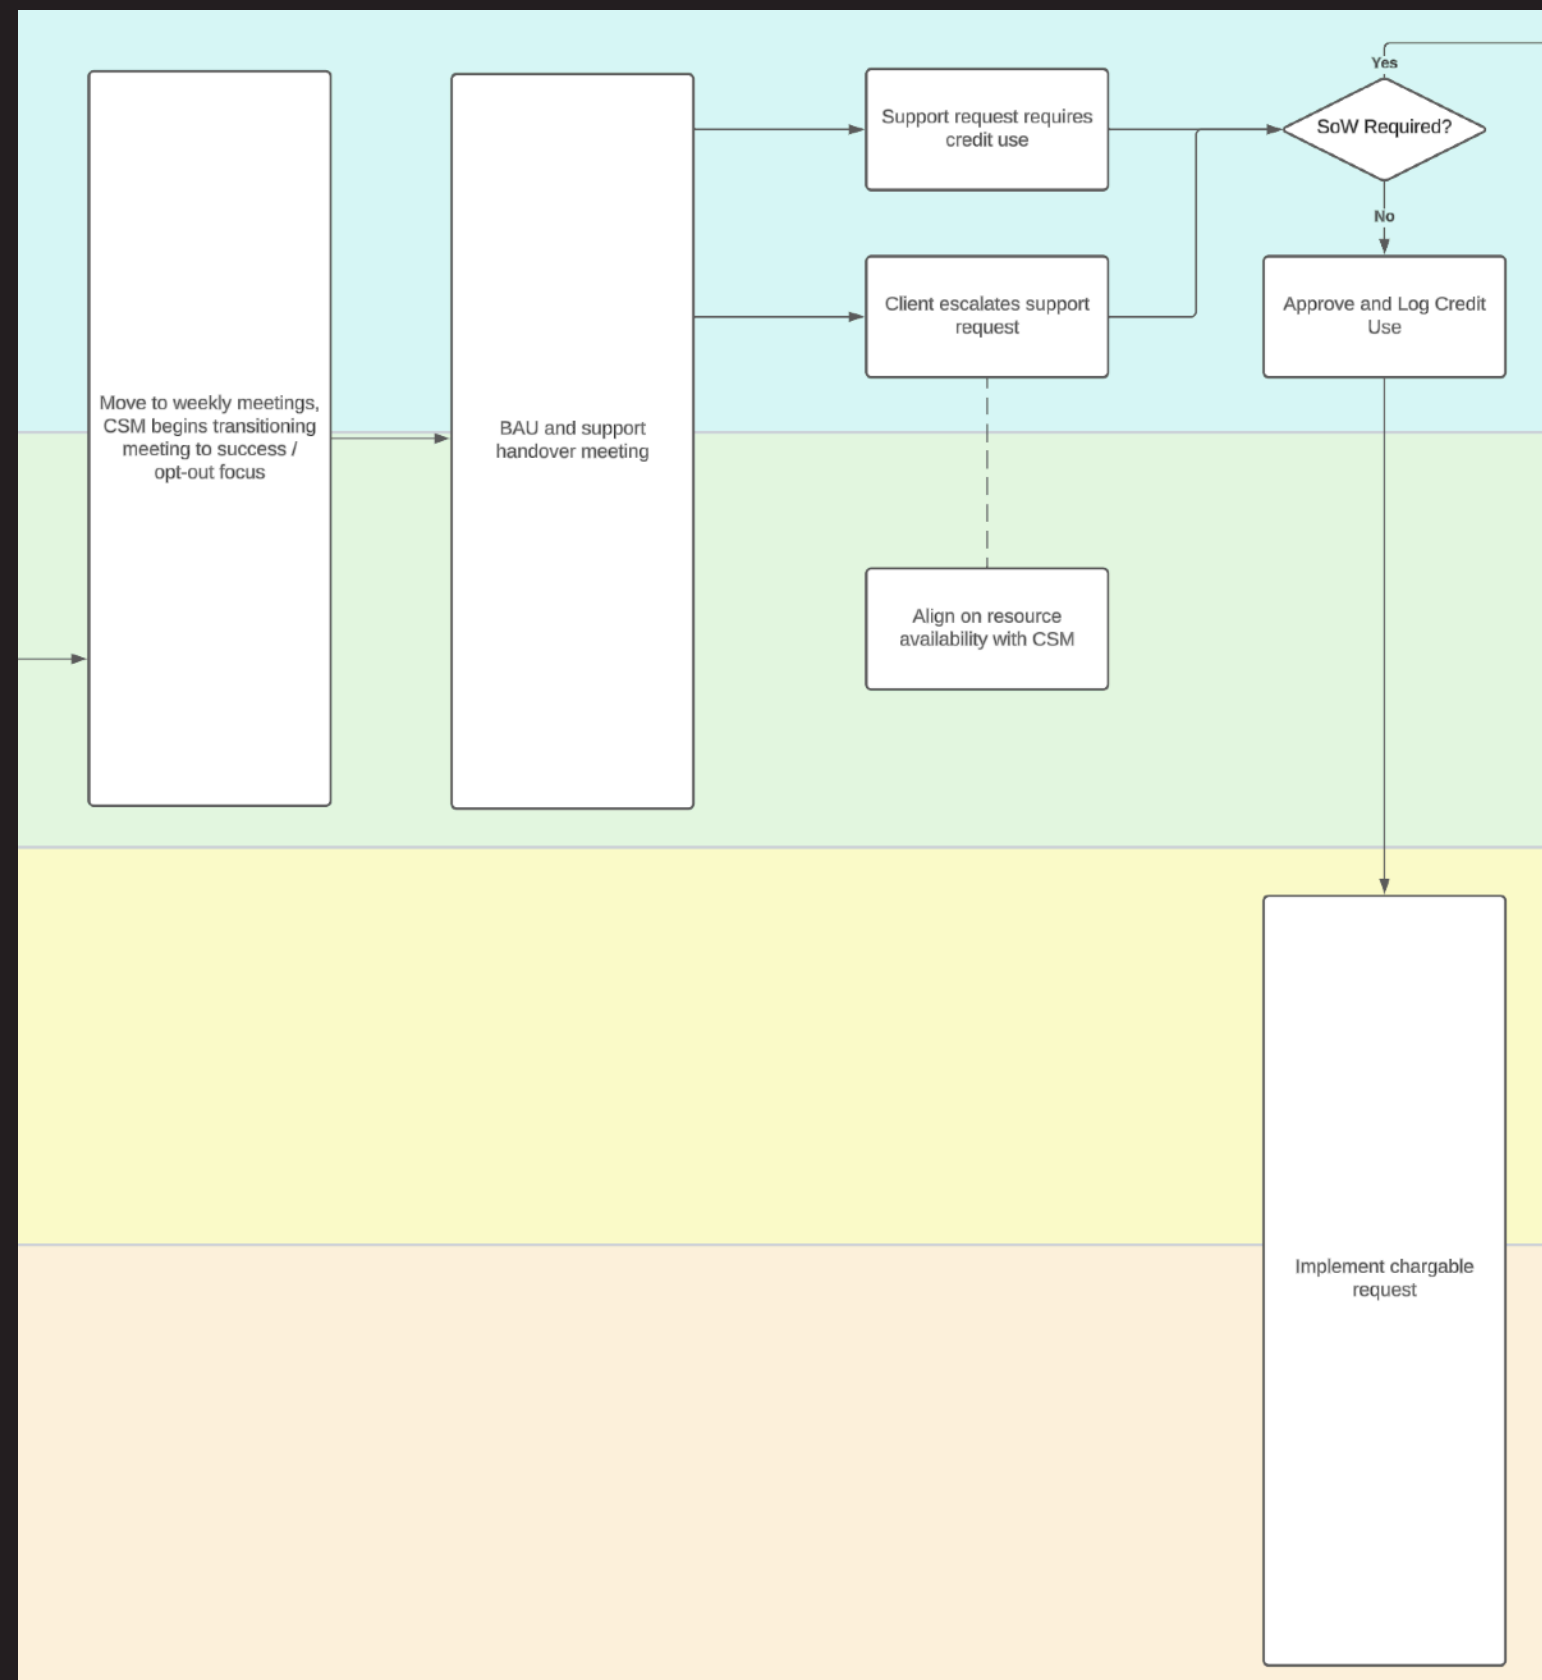

## CSM Increasing their Role

As the system is now build, the CSM will increase their role, leading more meetings. They should have been present throughout the build, but now will take an active role in ensuring the customer is fully enabled for BAU, and is confident about their ROI.

## Criteria to Exit Hypercare


This criteria is in the kickoff deck, and should be adhered to.

## Support

For detailed information on the support process, you should look at the support playbook. [🔗](#)

🔄 For smaller accounts, we are implementing a credit system, reflected in the diagram. Requests for changes will use a credit allowance. This is managed by the CSM and support.

# Deployment Process: Shifting to BAU




## QBR/MBR

For clients who are larger, there will be a monthly recap meeting set up by the CSM. The CSM and PSM work together to collate the releases from the past month, metrics, and suggested improvements.

Please see CS guidance on how to lead these meetings.

## Upsell / Renewal Procedure

Docs coming soon.

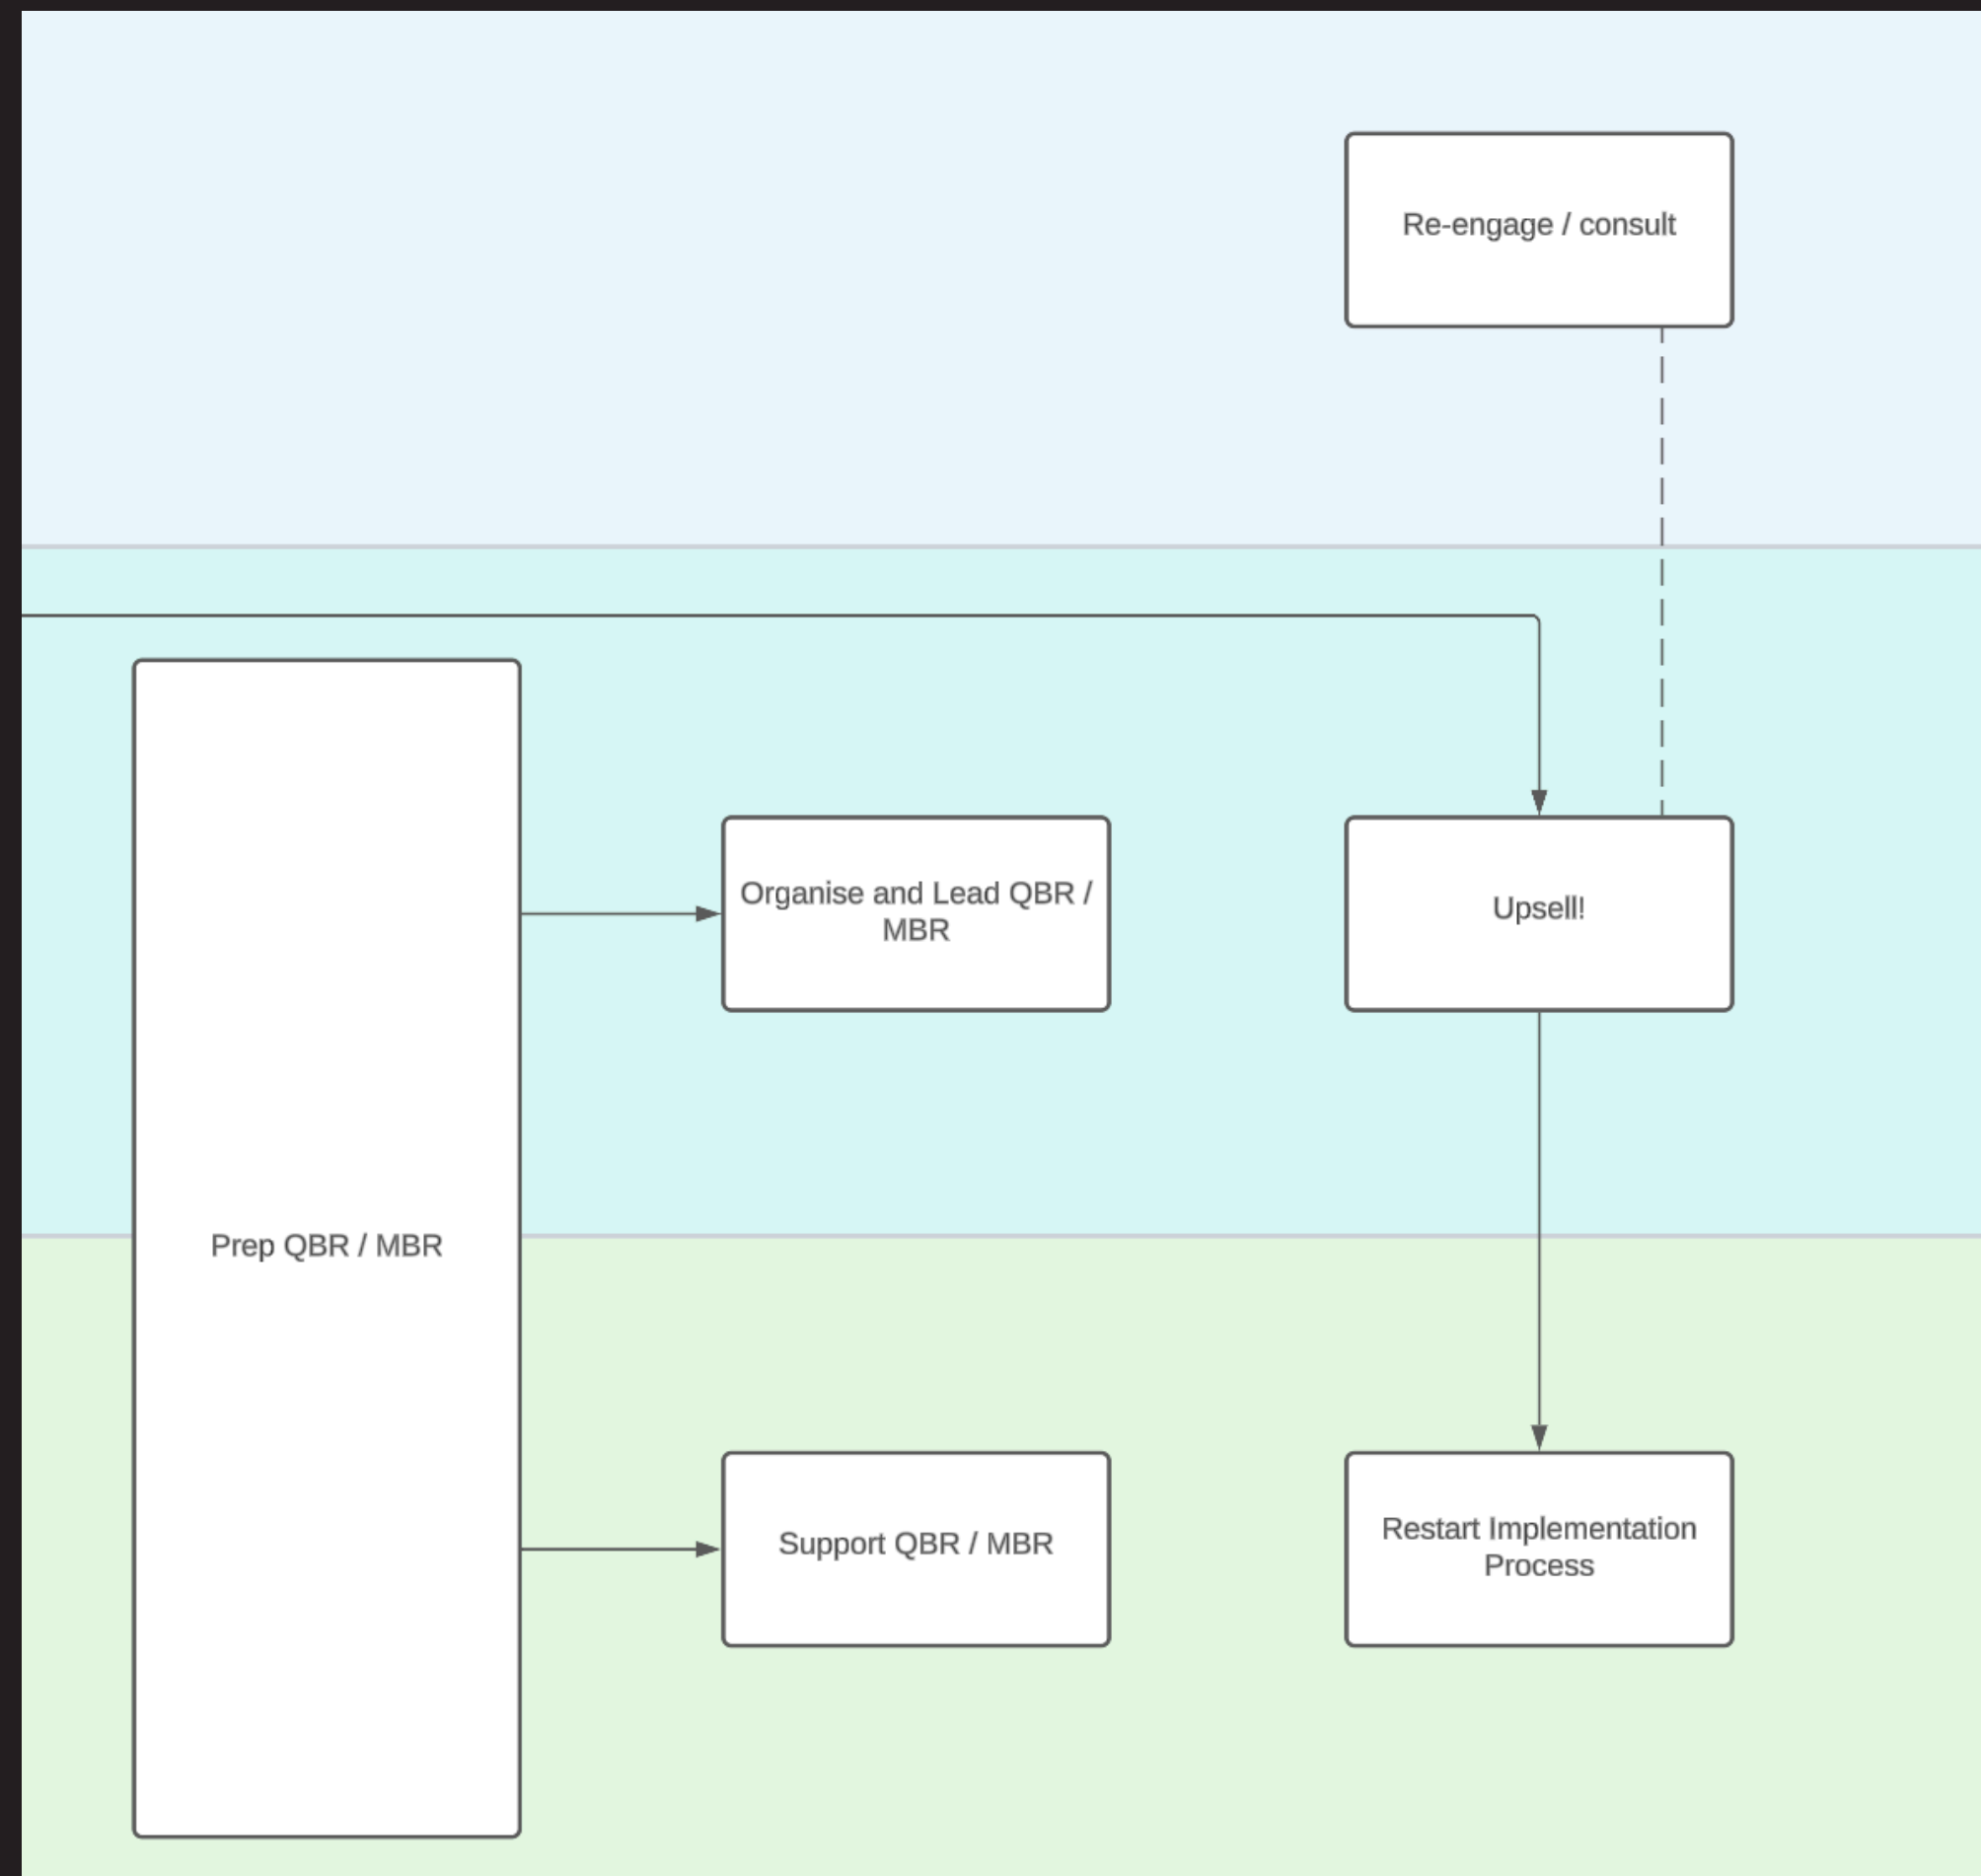



# In Depth: The Kickoff Meeting

The next slides will run through how to run a project kickoff. This is the PSM's first meeting with the client.


Overview

Introductions

## Introductions

You'll be assigned a dedicated support team for the duration of the design and build, to long term support.

### Your First Point of Contact



**Rob Baron**  
Product Solutions  
Manager

**Eshan Singhal**  
Software  
Engineering Lead

### Your Development Team

**Dialogue Designer**  
Responsible for the sound and customer experience of your virtual agent

**Engineering Team**  
Runs integrations, telephony, and ML and AI training

**Customer Success Manager**  
Leads steady state support for your virtual agent after go live



The introduction slide is straightforward.

The PSM is the main contact for the deployment, and the client should reach out to you primarily. That avoids miscommunication. It's also a good time to get a single point of contact from the client.

You'll want to introduce anyone else on the call in addition to the concept of a Agent Designer and a customer success manager — there for long term support.

You must change this slide depending on the project. Some will not have a CSM, so you can remove that.



# In Depth: The Kickoff Meeting

You should walk through a very high level view of what the agent will do. What is it meant to do from a high level — deflect calls from a contact centre or resolve a call type?

Read the order form before the meeting and be confident in what the customer is looking to do.

There will be a more detailed scope run through, so no need to dwell on this for long.

Overview

Your Virtual Agent

## Your Virtual Agent

We build in phases, so need to align on what we are launching together first to ensure maximum impact

When does your pool open for the season?

**Frequently asked Questions**

Answer customer service calls for simple requests, such as parking, opening hours, and directions.

Can I speak to Housekeeping?

**Routing to Departments**

Helping your PBX operators route calls to the right team

I need to speak to my host Parry Thomas

**Routing to Staff Members**

Recognise staff member names, and route the customer directly to them

